



14th Street Streetscape Project N.W. From
Thomas Circle to Florida Ave
DC Contract No.: DCKA-2016-C-0043

FAP No.: STP-2016 (054)

**CONSTRUCTION MANAGER'S
WEEKLY PROGRESS REPORT**

04/05/2020 - 04/11/2020

Project Website: www.14thstreetproject.com



Long Fence was on site working on handrails for the bus islands

PREPARED BY **Kendry A. Contreras**

A handwritten signature in blue ink, appearing to read 'Kendry A. Contreras'.

1. EXECUTIVE SUMMARY

Project Description:

The scope of the construction work includes the followings:

- The removal and disposal of existing roadway pavement, curb and gutter and sidewalks, milling of existing asphalt pavement to the extents shown on plans.
- The resurfacing of existing asphalt pavement using 2" Superpave AC surface on 14th Street between Thomas Circle and Florida Ave as shown in the plans.
- The replacement of all curbs and gutters with Granite Curbs, 12" Brick Gutter, Concrete Sidewalk, Wheelchair/Bicycle Ramps, and Cobble Stone LID Paver, Bioretention Planters as shown on the plans or as directed.
- The removal and transportation to storage yard of Existing Traffic Signals and Light Poles as shown on plans. Traffic signal relocation and equipment upgrading of Traffic Signals at all intersections of 14th Street within the project limit as shown on plans.
- Streetscaping throughout the 14th Street corridor as shown in the plans.
- The installation of traffic signing and permanent pavement markings.
- Upgrading of street lighting throughout the 14th Street corridor as shown in the plans.
- Construction and upgrading of single catch basin, double catch basin, and triple catch basin.
- Construction / Upgrading of new Watermains, Fire Hydrants
- Full Reconstruction of R Street.
- Installation of new Bus Islands and bus pads as shown on the plans and as directed.
- The installation and use of erosion and sediment control measures as required.
- Mobilization and demobilization, performance of field layout, provision and maintenance of engineer's field facilities, progress photographs, and the proper maintenance of vehicular and pedestrian traffic during construction, including provision of all required construction warning and detour signs and traffic control devices.

2. STATUS OF CONSTRUCTION / PROGRESS SUMMARY

Progress Summary:

1. No progress on 12" water main tie-in still on hold by DCwater. Ok to perform the shutdown the following week on Wednesday night
2. Placed Inlaid green markings
3. Splicing Streetlights
4. Continue pulling Comm system cable from 15th and 13th To Florida Ave.
5. Try to do a switchover at Florida. Conduit is broken DDOT notified
6. Omni continue parging and cleaning their inlets
7. Permanent Parking lanes/ Bike lanes. Layout
8. Plant additional trees along the corridor, mulch and Plant soil
9. Handrail installed at T street island
10. D.E.N. working on punchlist work

PM Community Outreach Activities:

11. TBA personnel continues to respond to questions that come through project portal.
12. Continue working with Businesses along T-u Block and sidestreets Including milli and paving operations
13. Reply to public concerns regarding the Corona virus

3. QC/ ISSUES / ACTION ITEMS

- DCwater still has one more tie-in to complete the DCWater/Pepco change order work. They need to schedule but currently all shutdown are on hold due to Coronavirus emergency proclamation. Agreement was reached to allow the shutdown on Wednesday 04/15
- Final Punchlist for D.E.n. issued on 04/06 They began working on it all week.
- Issue with Comm cable that is too big still waiting for Florida switchover
- Omni began punchlist of their structures
- FMCC needs additional resources to complete the punch lists and all work related to the project by the April 30th deadline
- Need resolution on change order # 9 Maxcell

ACTION ITEMS. -

Action	Description	Action By	Original Date	Expected Date	Status
001	Address the MOT, safety issues within the corridor.	FMCC/Kevin Felix	June 5, 2019	April 14, 2020	Ongoing
002	Contact Mr. Jermaine Quattlebaum and complete the punch list for DC Water work.	CM Team and DC Water/ Jermaine Quattlebaum	August 06, 2019	April 14, 2020	Ongoing
003	Showing DDOT the price difference of the luminaire with and without the glare shield.	FMCC Electrical	January 21, 2020	April 14, 2020	Ongoing
004	Submit the price proposal for reinstall of the blue historical signs	FMCC/Abdalla Elsheikh	January 21, 2020	April 14, 2020	Ongoing
005	Discussed internally for change order of the HAWK signal	FMCC Electrical	February 4, 2020	April 14, 2020	Ongoing
006	FMCC to remove all the trees per plan to allow Cooper Enterprise to continue the planting	FMCC/Abdalla Elsheikh	February 4, 2020	April 14, 2020	Ongoing

4. MEETINGS/ PROJECT COORDINATION

- New Progress Meeting are schedule via teleconference every other Tuesday at 10:30am.
- A meeting was held at Ellisdale work zone on 04/08 to discuss damage to curb. Mr. Proctor from Public space was present. Ellisdale denies any wrongdoing and accuses FMCC that when they were paving and repairing the sidewalk their crews had equipment on site

5. DAILY WORK PERFORMED

Monday 04/06/2020

FMCC was onsite providing MOT devices for work including:

- Cable work at Wallace Street parking and right lane.
- Inlaid thermoplastic pavement at W Street.
- DC-Line striping work starting at Florida Avenue.
- Long Fence handrails work at bus islands at R Street and T Street NW

FMCC Electrical crew was onsite working on cable installation along the corridor, starting at Wallace Street.

FlexiPave was on site installing Inlaid thermoplastic pavement at east side of W Street.

DC-Line worked on striping work, starting at Florida Avenue NW going south.

Long Fence was noticed onsite working at the bus islands at R Street and T Street NW installing handrails.

Ellisdale was noticed working on the sidewalk using the heavy equipment over the bus island in front of the building.

Tuesday 04/07/2020

FMCC was onsite providing MOT devices for work including:

- Electrical work along the corridor.
- DC-Line striping work starting near Rhode Island Avenue and Corcoran Street.
- Bike rack installation along the corridor as the result of the final walkthrough.
- Placing more mulch and top soil to the tree zones along the corridor.

FMCC Electrical crew was onsite working on cable installation along the corridor, also removed pole R87.

DC-Line worked on striping work, starting at Rhode Island Avenue and Corcoran Street going north.

FMCC Civil Crew was on site working on installation of the bike racks along the corridor based on the plans provided by the CM Team.

Cooper Enterprises worked on the site along the corridor placing more mulch and topsoil to the tree zones.

Wednesday 04/08/2020

FMCC was onsite providing MOT devices for work including:

- Striping parking lanes from Corcoran to N Street
- Communications system operations at Florida Street

FMCC Electrical crew was onsite Pulling Comm cable along Florida street from 15th Street to 14th Street. They Closed the road per authorization from DDOT.

FMCC Civil Crew was on site working on installation of the bike racks along the corridor based on the plans provided by the CM Team. Installed 15 Bike racks on missing spots, begin pouring bases for missing benches

Cooper Enterprises worked on the site along the corridor placing more mulch and topsoil to the tree zones. Planted 9 trees, Fixed plant soiled placed too high in bio retention planters.
Mulch- Various Locations –

DC Line showed up and worked at 14th Street Going south from Corcoran street south doing Parking lane spaces hatching and double yellow

DDOT had a cleaning crew in the field office performing surface deep cleaning.

Thursday, 04/09/2020

FMCC was onsite providing MOT devices for work including:

- Communications system operations at Florida Street

FMCC Electrical crew was onsite Pulling Comm cable along Florida Street from 13th Street to 14th Street. They Closed the road per authorization from DDOT. Discovered a broken Conduit. Harvey group notified it will be repaired today by MC dean

FMCC Civil Crew was on site working on installation of the bike racks along the corridor based on the plans provided by the CM Team. Installed 7 Bike racks on missing spots and 2 benches

Cooper Enterprises Fixed plant soiled placed too high in bio retention planters (Structural soil was too high).

Friday, 04/10/2020

FMCC was onsite providing MOT devices for work including:

- Communications system operations at Florida Street
- Lane closure for D.E.N

FMCC Electrical crew was onsite Pulling Comm cable along Florida Street from 13th Street to 14th Street. MC dean fixed the broken conduit but didn't installed mule tape, will finish splicing tomorrow

FMCC Electrical Crew was swapping HPS light fixtures for LED Fixtures at the block of V-W

D.E.N.- Was onsite completing Punchlist Items (Cracked sidewalk) Various locations.

Omni.- Was onsite cleaning Inlet structure near RIA. They are not coordinating with DC water.

Saturday, 04/11/2020

14th street N.W: FMCC provided MOT Devices for work safety:

DC Line continued to place permanent lane markings along the corridor of 14th street
FMCC Electrical team started to install the T base for the streetlight poles

7. RFI's/SUBMITTALS

1. Requests for Information:

- To date, we have received **51** RFIs; **49** RFIs have been answered.
- Glare shield RFI submitted to streetlight division. Waiting for copy of invoice
- FMCC submitted RFI about Maxcell

2. Submittals:

- We have received **87** Submittals; **87** Submittals have been Approved.

8. CHANGE ORDERS/TASK ORDERS

- Price breakdown for add water work received from FMCC. Tie-in were priced separately. Pepco sent letter on 12/14 accepting and taking responsibility of the CO. Sent Article 3 letter to FMCC on 12.20. Received commitment from DCwater to write Change. Quantity for Tie-in was estimated. Modification paperwork provided to FMCC for their signature
- FMCC Submitted a change order for 100K for max cell innerduct installed with fiber optic. Awaiting review from Wasim and Harvey group to check if it has merits, should be paid and direction. FMCC revised cost to only 50K
- Extended OH cost . Waiting for FMCC to provide justification and breakdown
- Work with DDOt in providing MOD 5 to ATCS to cover part time in June cost for CM and OE

9. DBE or CBE PARTICIPATION SUMMARIES

3. ATCS CBE / DBE Activity:

- Hayat Brown LLC.: Provided Office Engineering and Inspection support for this project.
- Cube root: Provided Inspection support
- Tina Boyd- PR and Outreach support, webpage management

4. Fort Myer Construction Corp. DBE Activity:

- Omni Excavators Inc.
- Den United LLC.
- DC Line
- Cooper landscaping
- Long Fence
- Capital Flexible pavement
- Driveway impressions


10. ACCIDENTS/INCIDENT

No incidents to report. FMCC was reminded to maintain DC emergency procedures to prevent the transmission of Co-vid19. AMtt Hill (FMCC VP) was on site enforcing the social distancing requirements

11. PHOTOS OF WORK PERFORMED THIS PERIOD




FMCC Electrical Crew on site working at Wallace Street

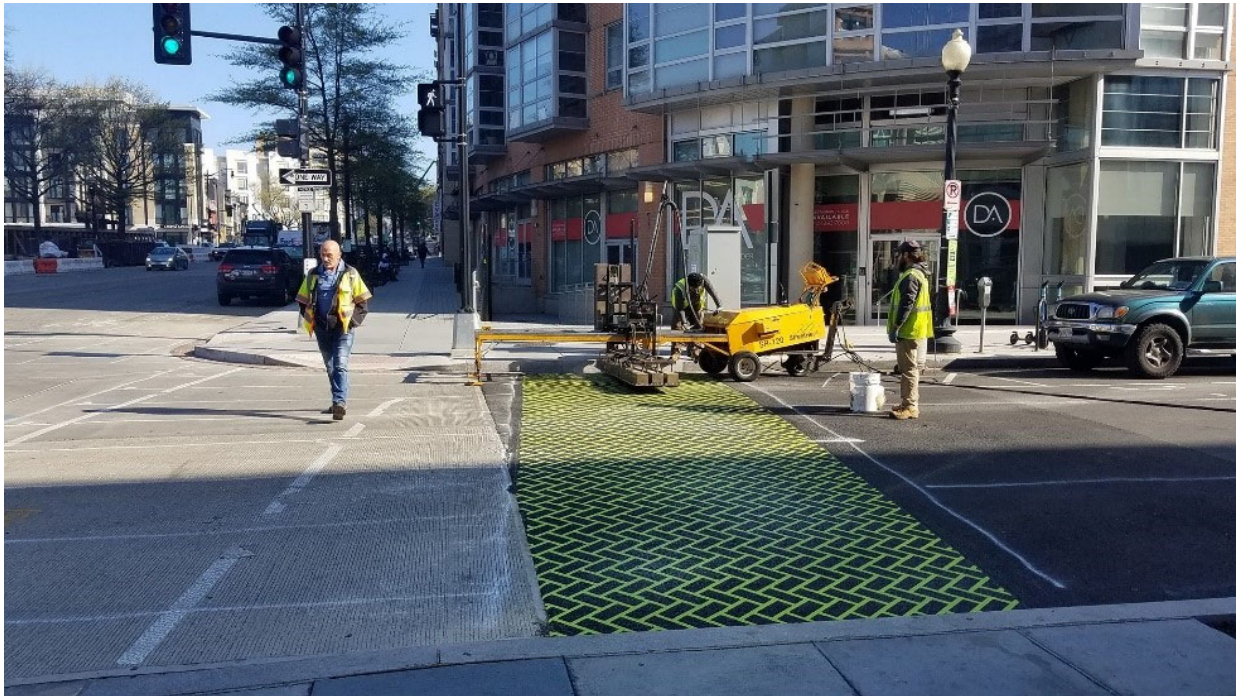

FlexiPave was on site working with the inlaid thermoplastic pavement



Cooper Enterprise was onsite placing mulch along the corridor

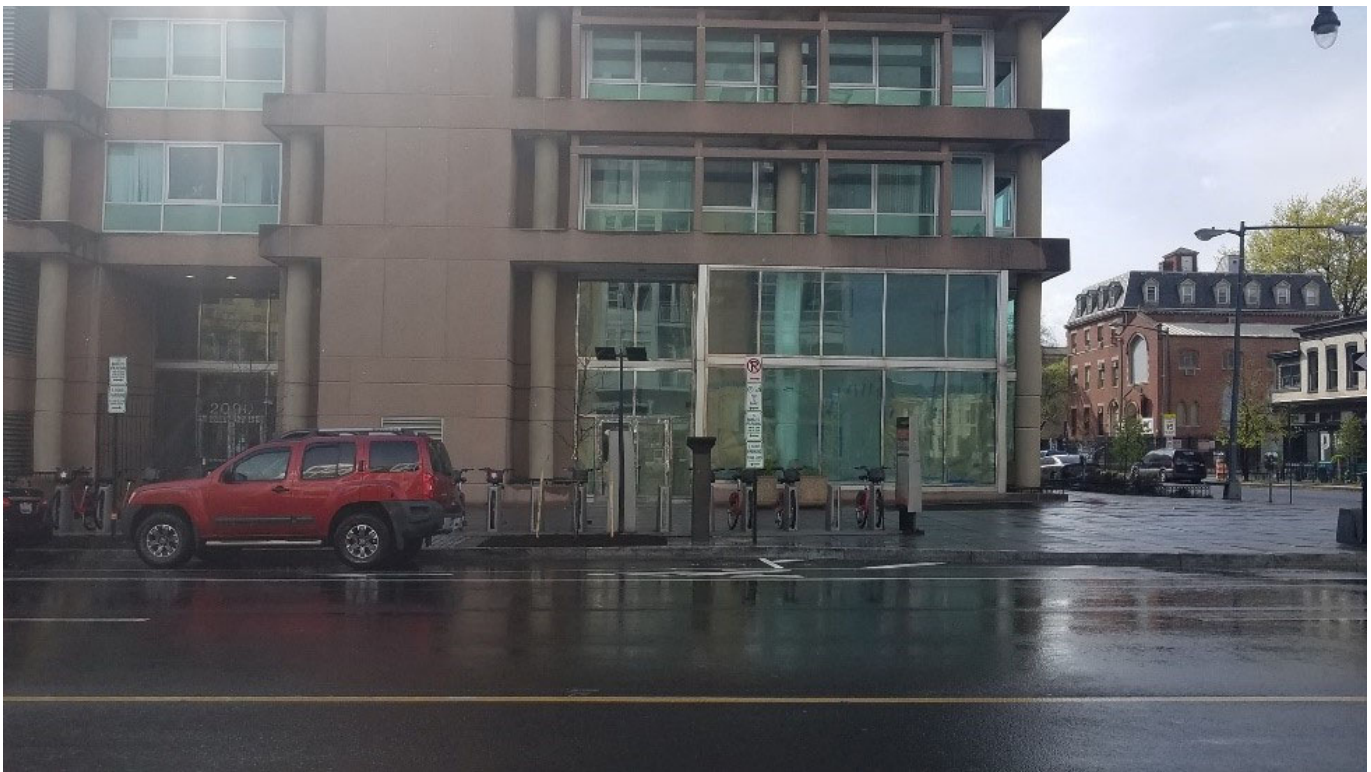

Parking meter installed at the SWC of V Street



Cooper Placing Mulch near bio retention # 3



Cooper augering for trees



Pulling Comm Cable Florida avenue West side



Installation of Bike Racks NEC Q street



Electrical Crew at Florida, Pulling Comm Cable



FMCC crew near T street installing missed Bike racks




Areas prepared by DEN for concrete




Electrician Swapping Light fixtures



Omni Cleaning Catch basin

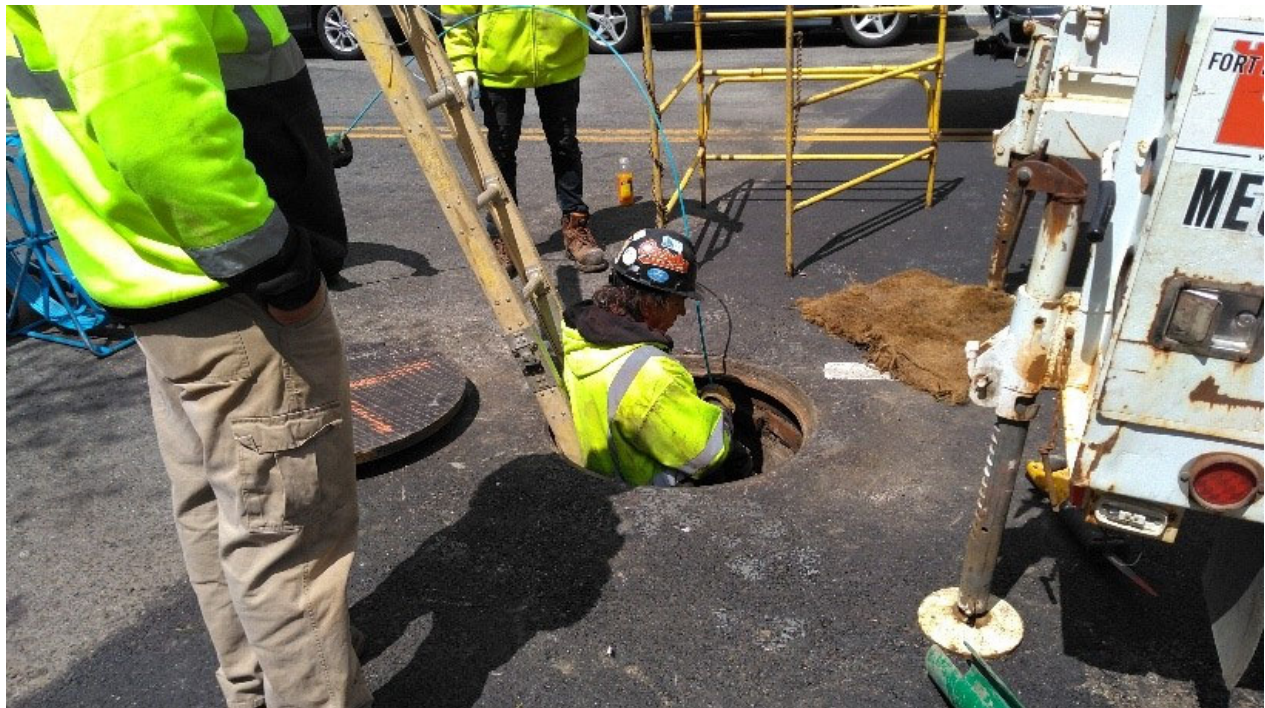

FMCC Electrician Pulling Comm Cable

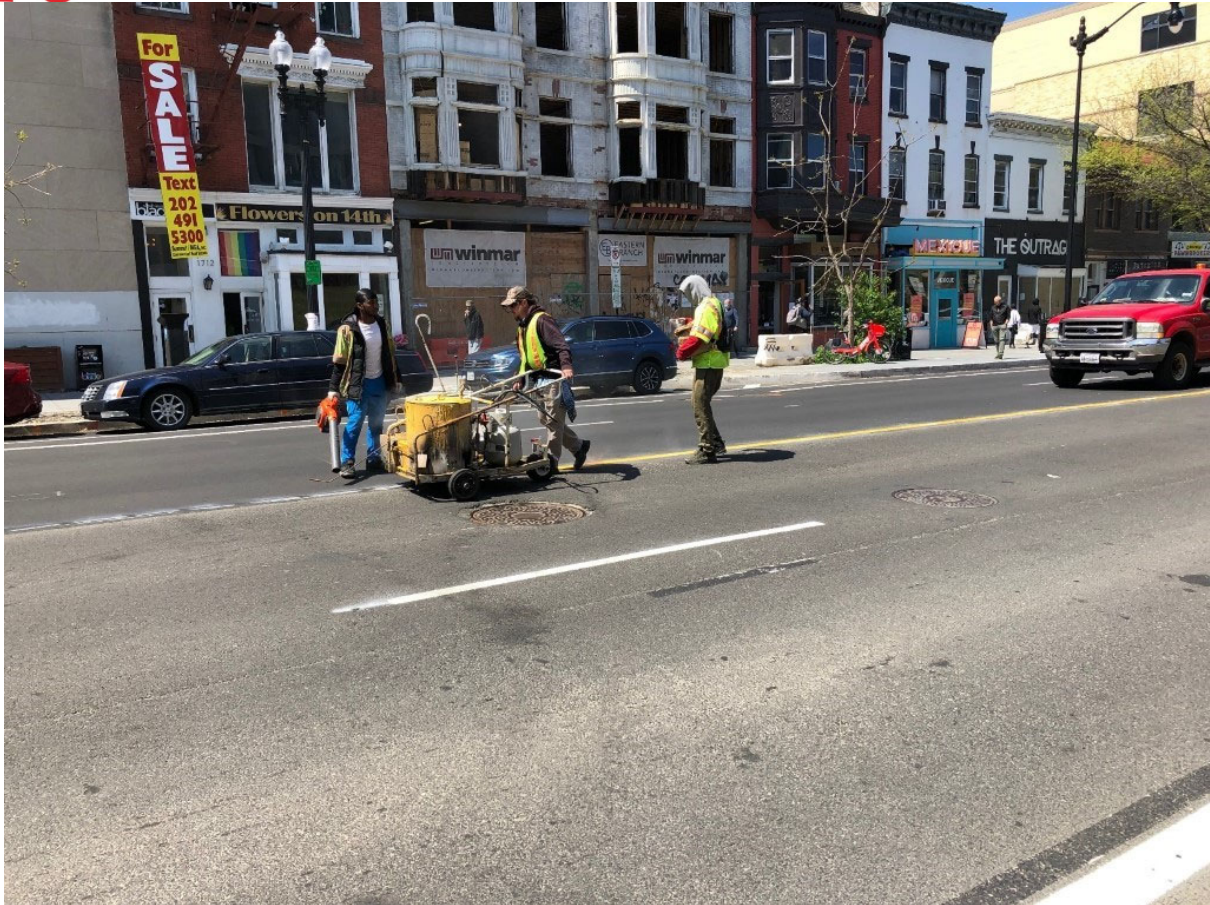

DC Line working on placement of Lane markings
