

**14th Street Streetscape Project N.W. From
Thomas Circle to Florida Ave
DC Contract No.: DCKA-2016-C-0043**

FAP No.: STP-2016 (054)

**CONSTRUCTION MANAGER'S
WEEKLY PROGRESS REPORT
12/08/2019 - 12/14/2019**

Project Website: www.14thstreetproject.com



OMNI: inlet Installation at T St NW

PREPARED BY Kendry A. Contreras

1. EXECUTIVE SUMMARY

Project Description:

The scope of the construction work includes the followings:

- The removal and disposal of existing roadway pavement, curb and gutter and sidewalks, milling of existing asphalt pavement to the extents shown on plans.
- The resurfacing of existing asphalt pavement using 2" Superpave AC surface on 14th Street between Thomas Circle and Florida Ave as shown in the plans.
- The replacement of all curbs and gutters with Granite Curbs, 12" Brick Gutter, Concrete Sidewalk, Wheelchair/Bicycle Ramps, and Cobble Stone LID Paver, Bioretention Planters as shown on the plans or as directed.
- The removal and transportation to storage yard of Existing Traffic Signals and Light Poles as shown on plans. Traffic signal relocation and equipment upgrading of Traffic Signals at all intersections of 14th Street within the project limit as shown on plans.
- Streetscaping throughout the 14th Street corridor as shown in the plans.
- The installation of traffic signing and permanent pavement markings.
- Upgrading of street lighting throughout the 14th Street corridor as shown in the plans.
- Construction and upgrading of single catch basin, double catch basin, and triple catch basin.
- Construction / Upgrading of new Watermains, Fire Hydrants
- Full Reconstruction of R Street.
- Installation of new Bus Islands and bus pads as shown on the plans and as directed.
- The installation and use of erosion and sediment control measures as required.
- Mobilization and demobilization, performance of field layout, provision and maintenance of engineer's field facilities, progress photographs, and the proper maintenance of vehicular and pedestrian traffic during construction, including provision of all required construction warning and detour signs and traffic control devices.

2. STATUS OF CONSTRUCTION / PROGRESS SUMMARY

Progress Summary:

1. Slow week due to inclement/ rainy weather (lost 3 days)
2. DEN performing punchlist of extensive areas of cracked sidewalk,
3. DEN Completing Bio retention Planter # 2, Completed Trench Darin at Riggs St.
4. Electricians Continue with work on Light poles and pulling cable
5. Addressing Punchlist of items at Rhode island
6. FMCC electrical continue pulling fiber optic comm cable and getting signal its components
7. Verizon moving the two manholes near R street, mobilize back form the top of slab waiting to finish the concrete slab.
8. Landscapers- Cooper continue demobilized
9. Omni continues building brick manhole in front of Winmar development (North of R street west side)
10. FMCC continued working on bike racks, benches and trash cans
11. Omni installed Storm drain at the NW corner of T and 14th Street

CM Community Outreach Activities:

12. TBA personnel continues to respond to questions that come through project portal.
13. Continue working with Businesses along R St. block. Red light Bar, Sette Osteria
14. PR team will continue with a report to the affecting communities of upcoming night work
15. Meeting with owner of Barcelona Wine for Basement flooding

3. QC/ ISSUES / ACTION ITEMS

- Developer Ellisdale at Florida and 14th Street didn't vacate, Public space lifted Stop work order. Ellisdale requested work to be pushed to 12/16 because of weather impacts.
- Bioretention Planter # 3 didn't have an outfall connecting to the storm drain causing mild flooding to the Barcelona Wine and Bar restaurant.
- DC water/ Pepco Conflict still hindering progress at the block of T and U street.
- Work by Omni is now part of the critical work, more resources are needed, storm drain going too slow
- Coordinating with Verizon for their manhole offset near R street ongoing.
- Multiple areas are unfinished that prevents the landscapers from completing their work (i.e. Cobble stone, PCC sidewalk, light pole and foundations).
- Omni working too slow is impacting other activities at R street
- PEPCO has all power feeds done. All traffic signal except for Florida done. FMCC missed a duct bank they need to install first. See bulletpoint below
- Comm conduit beyond Florida Ave. is full of sand. Harvey (DDOT signal) is aware of the issue.
- FMCC didn't installed duct bank at Florida Ave. They need to go back and install it
- FMCC has provided more resources but their subcontractors haven't
- Water work tie-waiting to locate the switch off valves (they were paved over by FMCC)

ACTION ITEMS.-

Action	Description	Action By	Original Date	Expected Date	Status
001	Address the MOT, safety issues within the corridor.	FMCC/Kevin Felix	June 5, 2019	December 17, 2019	Ongoing
002	Submit bus shelters Clear Channel full acceptance documentation.	FMCC/John Constantino	June 14, 2019	December 17, 2019	Ongoing
003	Provide written document showing the potential danger with the installation of the handles for the grate placed IFO Cleaners at 1329 14 th Street	FMCC/John Constantino/Cesar Casanova	July 30, 2019	December 17, 2019	Ongoing
004	Provide more samples for the cracked granite for the 1520 14 th Street owner acceptance.	FMCC/John Constantino	July 30, 2019	December 17, 2019	Ongoing
005	Mr. Said Chestnut to contact Mr. Jermaine Quattlebaum and start punch list for DC Water work.	ATCS/Said Chestnut and DC Water/ Jermaine Quattlebaum	August 06, 2019	December 17, 2019	Ongoing
006	Schedule a meeting with IPMD for the discussion about parking meter/Zip car signs	CM Team	September 10, 2019	December 17, 2019	Ongoing
007	Provided Long Fence documentation showing handrail quantity overrun	FMCC/Abdalla Elsheikh	October 8, 2019	December 3, 2019	Ongoing

008	Discuss to see if DDOT can provide a waiver for the installation of thermoplastic pavement with contrast tape at W Street.	CM Team/DDOT	December 3, 2019	December 17, 2019	New
009	Get PEPCO commitment for DC Water watermain relocation price proposal.	DDOT	December 3, 2019	December 17, 2019	New
010	Provide an exact number of parking meter, benches and bike racks were to be installed where Collection 14 and Ellisdale were working on.	FMCC/John Constantino	December 3, 2019	December 17, 2019	New
011	Research who owns the blue historical signs.	Jerrell Johnson	December 3, 2019	December 17, 2019	New

4. MEETINGS/ PROJECT COORDINATION

- New Progress Meeting are schedule at the Field Office every other Tuesday at 10:30am.
- Meeting with Owner of Barcelona because his basement got flooded, the reason is because Bio retention # 3 outfall was not connected water seep through a sinkhole and flooded his basement. The meeting with FMCC and the Owner was very productive and there was an agreement from the contractor to resolve the connection ASAP
- Winmar developer and Ellisdale developer has been coordinating with the project to provide access

5. DAILY WORK PERFORMED

Monday 12/09/2019

FMCC Electricians: The electricians started splicing the 4/0 cable in the manhole M30 at Q Street. The electricians installed the (2) EA 100 Watt post top LED fixture with Washington Globe photocell.

Omni worked on manhole at 14th St. close to R St. NW. due to raining the contractor could not to continue the work and just completed a portion of the manhole .

FMCC cancelled work at approximately 10:30 Am due to rain.

Tuesday 12/10/2019

FMCC: Cleaned up the jobsite

FMCC Electricians: Finished splicing the 4/0 cable in manhole M40 at 14th Street NW and Q Street Installed (6) 100 Watt Post Top LED Fixture w/ Washington Globe and Photocell at Light pole

L-70, L-68, and L-67

Installed (2) Video Detection cameras at TS-03 and TS-01

The splicing crew cancelled work at 11:30 Am due to rain and the crew continued to work an eight hour day.

Omni: Due to raining, the contractor could not continue the work and just completed a portion of the manhole at 14 St NW close to R St NW .

Wednesday 12/11/2019

FMCC: Sawcut the existing roadway for the proposed 6" perforated pipe which runs from Bio-Retention Planter No-2 to an existing combined sewer manhole in front of 1728 14th Street NW.

DEN: Excavated, placed a vapor barrier, and formed the Bio-Retention Planter No.2 in front of 1738 SB 14th Street NW

DEN: Poured the remaining section of punch list 4" PCC Sidewalk.

FMCC placed, water filled jersey barriers, traffic drums, cones and arrow board at 14th & T St to R St for Omni Excavators trench work and D.E.N. excavation for planters.

FMCC installed traffic signals and pedestrian modules (TS-09) at SWC of 14th & Rhode Island Avenue following trimming of branches at tree.

Omni Excavators continued work at 1714 forming catch basin CB-18. Second crew worked at SWC of 14th & T St excavating for catch basin CB-25. Work is scheduled to continue tomorrow.

Thursday, 12/12/2019

FMCC placed, water filled jersey barriers, traffic drums, cones and arrow board at 14th & T St to R St for Omni Excavators trench work and D.E.N. excavation for planters.

FMCC installed traffic signals and pedestrian modules (TS-09) at SWC of 14th & Rhode Island Avenue following trimming of branches at tree.

Omni Excavators continued work at 1714 forming catch basin CB-18. Second crew worked at SWC of 14th & T St excavating for catch basin CB-25. Work is scheduled to continue tomorrow.

Friday, 12/13/2019

DEN: DEN cancelled work today due to rain.

FMCC cancelled work to rain.

Saturday, 12/14/2019

FMCC placed, arrow board at 14th & V St northbound FMCC Electrical Crew.

FMCC Electrical crew was onsite connecting cable from cabinet to traffic signal poles at SEC, NEC and SWC of 14th & V St. Work is scheduled to continue on Monday, December 16th.

7. RFI's/SUBMITTALS**1. Requests for Information:**

- To date, we have received **39** RFIs; **39** RFIs have been answered.

2. Submittals:

- We have received **85** Submittals; **85** Submittals have been Approved.
- Waiting for 2019 Concrete Mix designs

8. CHANGE ORDERS/TASK ORDERS

- FMCC to revise overhead cost (field office, MOT...) change order for 6 month contract extension. Received breakdown, FT Myers Accepted counteroffer, with DDOT to provide executed change order
- Waiting for ATCS MOD 3 Additional funding to continue inspection services in October
- Price breakdown for add water work received from FMCC. Tie-in were priced separately. Waiting for PEPCO to formally accept the amount

9. DBE or CBE PARTICIPATION SUMMARIES**3. ATCS CBE / DBE Activity:**

- Hayat Brown LLC.: Provided Office Engineering and Inspection support for this project.
- Cube root: Provided Inspection support

4. Fort Myer Construction Corp. DBE Activity:

- Omni Excavators Inc.
- Den United LLC.
- DC Line
- Cooper landscaping
- Long Fence

10. ACCIDENTS/INCIDENT

No incidents or accidents to report

11. PHOTOS OF WORK PERFORMED THIS PERIOD



The 100 Watt Post Top Fixtures were installed today at southbound 1738 14th Street NW



OMNI:manhole construction 14th St



OMNI:manhole construction 14th St



FMCC installing the Post Top Fixtures at light pole L-67



FMCC splicing the 4/0 cable in manhole M40 at 14th Street NW and Q Street



DEN excavating for Bio-Retention Planter No.2



DEN forming Bio-Retention Pond No.2



DEN pouring the sidewalk at the NW corner of U Street and 2000 14th Street NW




FMCC installing traffic signal TS-09 at SWC of 14th & RIA following tree branch trimming



Omni excavating for installation of catch basin CB-25




Detection camera installed at NEC at 14th & N St

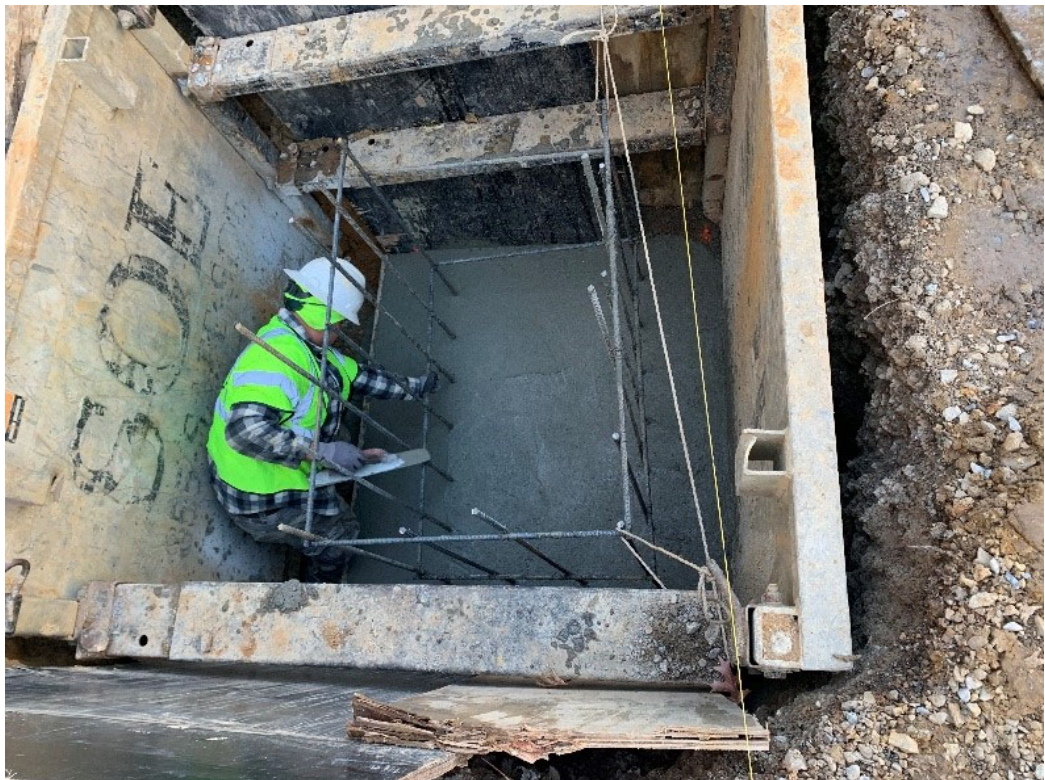

OMNI:manhole construction 14th St



OMNI: Inlet installation at T St NW

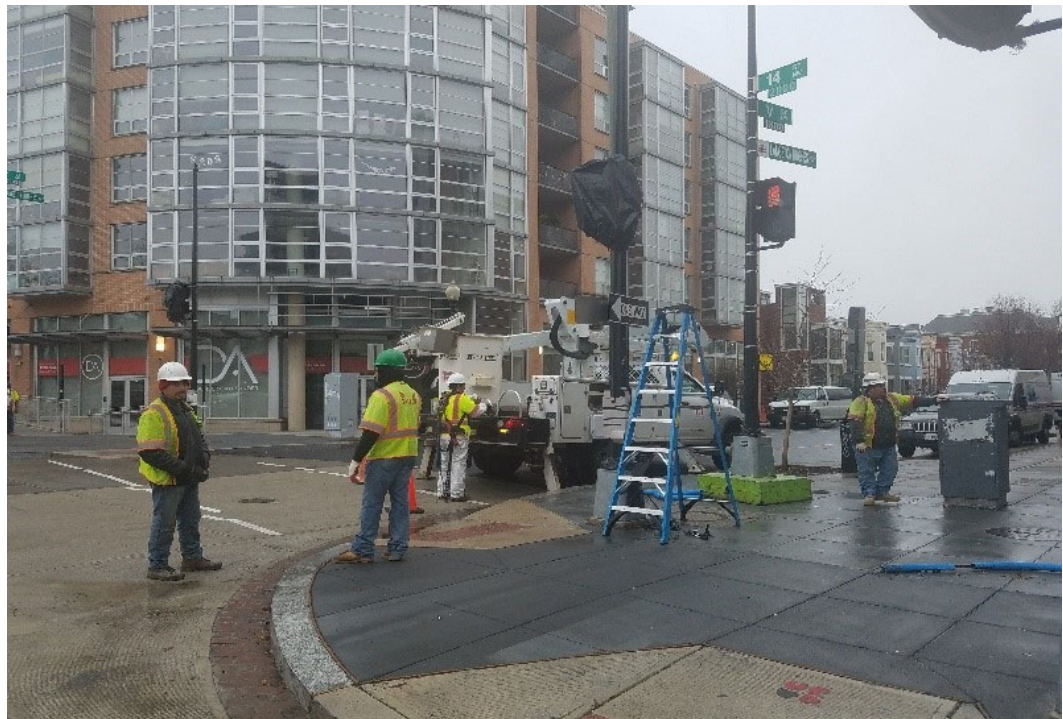

FMCC at SEC of 14th & V connecting cable at traffic signal



Cable being connected to LED module at NEC of 14th & V St.

