


**14<sup>th</sup> Street Streetscape Project N.W.**  
**From Thomas Circle to Florida Ave**  
**DC Contract No.: DCKA-2016-C-0043**

FAP No.: STP-2016 (054)

**CONSTRUCTION MANAGER'S**  
**WEEKLY PROGRESS REPORT**  
**11/26/2018 – 12/01/2018**

Project Website: [www.14thstreetproject.com](http://www.14thstreetproject.com)

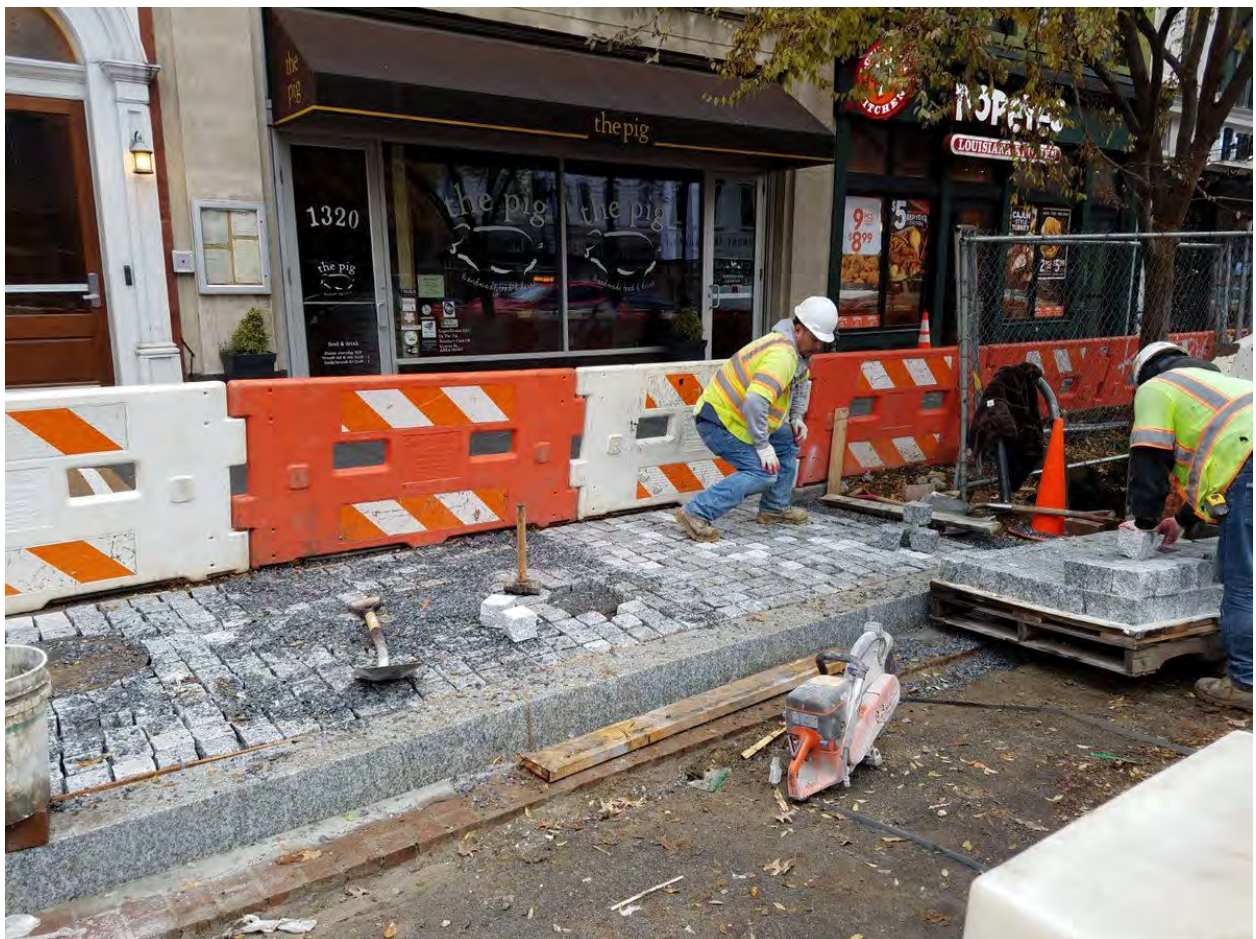

*Placement of Granite Cobble Stone between N Street and Rhode Island on the Westside*

## 1. EXECUTIVE SUMMARY

### Project Description:

The scope of the construction work includes the followings:

- The removal and disposal of existing roadway pavement, curb and gutter and sidewalks, milling of existing asphalt pavement to the extents shown on plans.
- The resurfacing of existing asphalt pavement using 2" Superpave AC surface on 14<sup>th</sup> Street between Thomas Circle and Florida Ave as shown in the plans.
- The replacement of all curbs and gutters with Granite Curbs, 12" Brick Gutter, Concrete Sidewalk, Wheelchair/Bicycle Ramps, and Cobble Stone LID Paver, Bioretention Planters as shown on the plans or as directed.
- The removal and transportation to storage yard of Existing Traffic Signals and Light Poles as shown on plans. Traffic signal relocation and equipment upgrading of Traffic Signals at all intersections of 14<sup>th</sup> Street within the project limit as shown on plans.
- Streetscaping throughout the 14<sup>th</sup> Street corridor as shown in the plans.
- The installation of traffic signing and permanent pavement markings.
- Upgrading of street lighting throughout the 14<sup>th</sup> Street corridor as shown in the plans.
- Construction and upgrading of single catch basin, double catch basin, and triple catch basin.
- Construction / Upgrading of new Watermains, Fire Hydrants
- Full Reconstruction of R Street.
- Installation of new Bus Islands and bus pads as shown on the plans and as directed.
- The installation and use of erosion and sediment control measures as required.
- Mobilization and demobilization, performance of field layout, provision and maintenance of engineer's field facilities, progress photographs, and the proper maintenance of vehicular and pedestrian traffic during construction, including provision of all required construction warning and detour signs and traffic control devices.

### Work by Others

The PEPCO manhole replacement or vault adjustments activities will be done by others approved by PEPCO. The ATCS CM team will coordinate all these activities with the Contractor and PEPCO.

## 2. STATUS OF CONSTRUCTION / PROGRESS SUMMARY

### Progress Summary:

1. Omni onsite excavating and installing electrical conduits and manholes
2. Omni is excavating and installing Traffic Signal and Street Light Foundations
3. DEN installing Granite Curb and Brick Gutter
4. DEN demoing and installing PCC Sidewalk
5. DEN installing Permeable Pavers (Granite Cobble Stones)
6. FMCC onsite providing MOT for Subcontractors

### CM Community Outreach Activities

1. Connected with retailers and property owners in project corridor to provide updates and address any questions or concerns.
2. Project Website is up and running. Responded to email questions that came through Project Website.

## 3. ISSUES / ACTION ITEMS

- Ongoing Issues / Items: Bus Shelter Removal, PEPCO Manhole conflicts

- New Issues / Items:
- Action Items: Pepco working on conflicts (approx. 26) and give CM a report on time frame for design and corrections.
- Spoke with Carla Longshore from DDOT TDD. Need to reach back out to get assistance with Clear Channel and getting the Street Car Shelters

## 4. MEETINGS / PROJECT COORDINATION

Progress Meeting are schedule at the Field Office every Tuesday at 10:30am

## 5. DAILY WORK PERFORMED

### Monday 11/26/2018

1. Den continued to install the Granite Cobble Stone between N Street and Rhode Island Ave
2. Omni cancelled its operation due the forecasted inclement weather
3. FMCC was onsite providing MOT for these operations

### Tuesday 11/27/2018

1. Den continued the replacement of the PCC Sidewalk between N Street and Rhode Island Ave
2. Den continued with the new Granite Curb and Brick Gutter installation at the NW corner of Rhode Island Ave
3. Omni continued to excavate and place 2" and 4" PVC conduit between P14 to TC-10, MH-96 to TC-10, Mh-96 to MH-95, MH-97 to MH-98
4. FMCC was onsite providing MOT for these operations.

### Wednesday 11/28/2018

1. Omni installed two (2) manholes MH-95, and MH-96 and began backfilling around these manholes
2. Den continued with the installation of Structural soil and PCC Sidewalk replacement between N Street and Rhode Island Ave
3. Den also continued to place Brick Gutter between N Street and Rhode Island Ave
4. FMCC was onsite providing MOT for these operations

### Thursday 11/29/2018

1. Den began replacement of the PCC Sidewalk at the NW corner of Rhode Island Ave
2. Omni removed the TS/SL foundation at the SE corner of P Street
3. Omni formed and placed the TCC cabinet at the NW corner of W Street
4. Omni continue installing 2" and 4" PVC Conduit between MH-94 to C68, MH-96 to MH-95, MH-97 to MH-98, MH-98 to L115
5. FMCC was onsite providing MOT for these operations

### Friday 11/30/2018

1. Den began the replacement of the Driveway entrance between N Street and Rhode Island on the Westside
2. Den also placed the ADA ramp at the SW corner of N Street
3. Omni placed Aggregate base and PCC Base between MH-94 to MH-95
4. Omni continued to install 2" and 4" PVC Conduit between Mh-94 to C68, C68 to L28, MH-94 to TS-11, and TS-12
5. FMCC as onsite providing MOT for these operations

## Saturday 12/01/2018

1. FMCC onsite cleaning up and moving barrier between N Street and Rhode Island Ave
2. FMCC Electrical was on site repairing the Street Light at the SE corner of 14<sup>th</sup> and P, and SE corner of 14<sup>th</sup> and Rhode Island Ave

## 6. INSPECTION & MATERIAL TESTS PERFORMED

- None

## 7. RFI's / SUBMITTALS

- Requests For Information:
  - o We have received 15 RFIs; 13 RFIs have been answered.
- Submittals:
  - o We have received 68 Submittals; 68Submittals have been Approved

## 8. CHANGE ORDERS/TASK ORDERS

- o None

## 9. DBE or CBE PARTICIPATION SUMMARIES

- ATCS CBE / DBE Activity:
  - o Hayat Brown LLC.: Provided Office Engineering support for this project.
- ATCS CBE / DBE Activity
  - o Cube Root, Corp.: Providing an Electrical Inspector to support the project.
- Fort Myer Construction Corp. DBE Activity:
  - o Omni Excavators Inc.
  - o Den United LLC.

## 10. ACCIDENTS / INCIDENTS

- None

## 11. PHOTOS OF WORK PERFORMED THIS PERIOD



*Placing PCC Sidewalk between N Street and Rhode Island Ave*



*Brick Gutter installation between N Street and Rhode Island Ave*



*Installation of PVC Conduit for Traffic Signal Foundation*



*Installation Manhole at the corner of 14<sup>th</sup> and W Street*
