

14th Street Streetscape Project N.W.
From Thomas Circle to Florida Ave
DC Contract No.: DCKA-2016-C-0043

FAP No.: STP-2016 (054)

CONSTRUCTION MANAGER'S
WEEKLY PROGRESS REPORT
12/31/2018 – 1/05/2019

Project Website: www.14thstreetproject.com



PCC Sidewalk Placement between P Street and Q Street

1. EXECUTIVE SUMMARY

Project Description:

The scope of the construction work includes the followings:

- The removal and disposal of existing roadway pavement, curb and gutter and sidewalks, milling of existing asphalt pavement to the extents shown on plans.
- The resurfacing of existing asphalt pavement using 2" Superpave AC surface on 14th Street between Thomas Circle and Florida Ave as shown in the plans.
- The replacement of all curbs and gutters with Granite Curbs, 12" Brick Gutter, Concrete Sidewalk, Wheelchair/Bicycle Ramps, and Cobble Stone LID Paver, Bioretention Planters as shown on the plans or as directed.
- The removal and transportation to storage yard of Existing Traffic Signals and Light Poles as shown on plans. Traffic signal relocation and equipment upgrading of Traffic Signals at all intersections of 14th Street within the project limit as shown on plans.
- Streetscaping throughout the 14th Street corridor as shown in the plans.
- The installation of traffic signing and permanent pavement markings.
- Upgrading of street lighting throughout the 14th Street corridor as shown in the plans.
- Construction and upgrading of single catch basin, double catch basin, and triple catch basin.
- Construction / Upgrading of new Watermains, Fire Hydrants
- Full Reconstruction of R Street.
- Installation of new Bus Islands and bus pads as shown on the plans and as directed.
- The installation and use of erosion and sediment control measures as required.
- Mobilization and demobilization, performance of field layout, provision and maintenance of engineer's field facilities, progress photographs, and the proper maintenance of vehicular and pedestrian traffic during construction, including provision of all required construction warning and detour signs and traffic control devices.

Work by Others

The PEPCO manhole replacement or vault adjustments activities will be done by others approved by PEPCO. The ATCS CM team will coordinate all these activities with the Contractor and PEPCO.

2. STATUS OF CONSTRUCTION / PROGRESS SUMMARY

Progress Summary:

1. Omni onsite excavating and installing electrical conduits and manholes
2. Omni is excavating and installing Traffic Signal and Street Light Foundations
3. Omni excavating and installing Catch Basins and Sewer Manholes
4. DEN installing Granite Curb and Brick Gutter
5. DEN demoing and installing PCC Sidewalk
6. DEN installing Permeable Pavers (Granite Cobble Stones)
7. FMCC Electrical Installing Traffic Signal Poles, Transformer Bases, and Pendent Poles
8. FMCC onsite providing MOT for Subcontractors

CM Community Outreach Activities

1. Connected with retailers and property owners in project corridor to provide updates and address any questions or concerns.
2. Project Website is up and running. Responded to email questions that came through Project Website.

3. ISSUES / ACTION ITEMS

- Ongoing Issues / Items: Bus Shelter Removal, PEPCO Manhole conflicts

- New Issues / Items:

- Action Items: Pepco working on conflicts (approx. 9) and give CM a report on time frame for design and corrections.

- Clear Channel provide a cost for removal, provided cost to DDOT PM

4. MEETINGS / PROJECT COORDINATION

Progress Meeting are schedule at the Field Office every Tuesday at 10:30am

5. DAILY WORK PERFORMED**Monday 12/31/2018**

1. Contractor cancelled all activities today due to Holiday Lane Closure restrictions

Tuesday 1/01/2019

1. Contractor did not work due to the Holiday restrictions

Wednesday 1/02/2019

1. DEN continued with the installation of PCC Sidewalk, Granite Curb, Brick Gutter, and Cobble Stone between P Street and Q Street on the Eastside
2. Omni continue installing the 2" and 4" PVC Conduit between V and U Street
3. Omni excavated and installed Catch Basin at 14th and Corcoran, and between Riggs and S Street
4. FMCC electrical furnished and installed five (5) Street Light Poles
5. FMCC was onsite providing MOT for these operations

Thursday 1/03/2019

1. Omni placed aggregate base and PCC Base over electrical trench for laterals between V and U Street
2. Omni continued to install 15" PCC connection pipes for Catch Basin at 14th and Q, and 14th and Swann
3. DEN continued with PCC Sidewalk, Granite Curb and Brick Gutter installation between P and Q Street on the Eastside
4. FMCC electrical placed 28.5' Pendent Poles
5. FMCC was onsite providing MOT for these operations

Friday 1/04/2019

1. Omni continue with the electrical laterals installing 2" PVC conduit between V and U Street
2. Omni excavated and poured three (3) Street Light Foundations
3. Den continued replacement of the PCC Sidewalk between P and Q Street on the Eastside
4. Den began excavation for the Bump out at Church Street
5. FMCC Electrical placed four (4) 150-watt LED Tear Drop Fixtures

- 6. FMCC was on site providing MOT

Saturday 1/05/2019

- 1. Contractor elected not to work today due to forecasted inclement weather

6. INSPECTION & MATERIAL TESTS PERFORMED

- 1/4/19 9 CY of Class B Concrete – Slump 4", Air 6.2%, 4 cylinders were made

7. RFI's / SUBMITTALS

- Requests For Information:
 - o We have received 15 RFIs; 14 RFIs have been answered.
- Submittals:
 - o We have received 68 Submittals; 68 Submittals have been Approved

8. CHANGE ORDERS/TASK ORDERS

- o CM Task Order Modification submitted to DDOT for time extension was approved

9. DBE or CBE PARTICIPATION SUMMARIES

- ATCS CBE / DBE Activity:
 - o Hayat Brown LLC.: Provided Office Engineering support for this project.
- ATCS CBE / DBE Activity:
 - o Cube Root, Corp.: Providing an Electrical Inspector to support the project.
- Fort Myer Construction Corp. DBE Activity:
 - o Omni Excavators Inc.
 - o Den United LLC.


10. ACCIDENTS / INCIDENTS

- None

11. PHOTOS OF WORK PERFORMED THIS PERIOD



Removal of Street Car Track between V and U Street

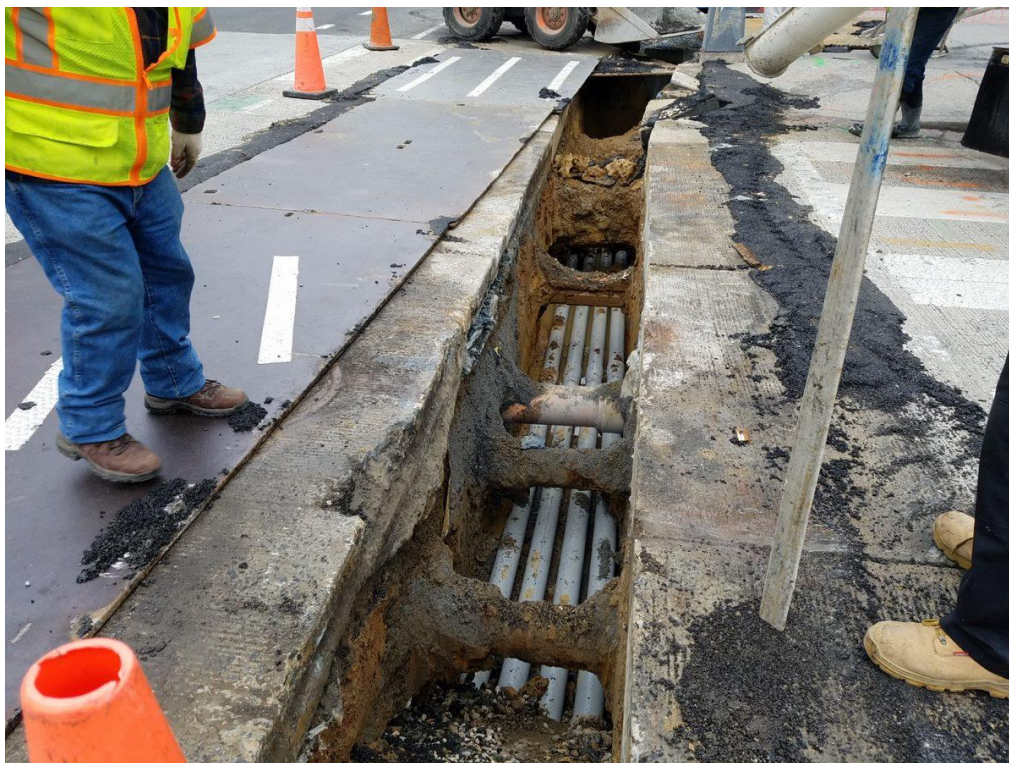

Installation of 4' PVC Conduit at the NE corner of V Street



Installation of Double Catch Basin at Swann Street



Excavation for installation of Structural Soil between P and Q Street



Installation of Granite Curb between P and Q Street



Installation of Brick Gutter between P and Q Street
