

14<sup>th</sup> Street Streetscape Project N.W. From  
Thomas Circle to Florida Ave  
DC Contract No.: DCKA-2016-C-0043

FAP No.: STP-2016 (054)

---

**CONSTRUCTION MANAGER'S  
WEEKLY PROGRESS REPORT**  
03/22/2020 - 03/28/2020

---

Project Website: [www.14thstreetproject.com](http://www.14thstreetproject.com)



14<sup>th</sup> St SB near R St asphalt placement underway

**PREPARED BY**      **Kendry A. Contreras**

## 1. EXECUTIVE SUMMARY

### Project Description:

The scope of the construction work includes the followings:

- The removal and disposal of existing roadway pavement, curb and gutter and sidewalks, milling of existing asphalt pavement to the extents shown on plans.
- The resurfacing of existing asphalt pavement using 2" Superpave AC surface on 14<sup>th</sup> Street between Thomas Circle and Florida Ave as shown in the plans.
- The replacement of all curbs and gutters with Granite Curbs, 12" Brick Gutter, Concrete Sidewalk, Wheelchair/Bicycle Ramps, and Cobble Stone LID Paver, Bioretention Planters as shown on the plans or as directed.
- The removal and transportation to storage yard of Existing Traffic Signals and Light Poles as shown on plans. Traffic signal relocation and equipment upgrading of Traffic Signals at all intersections of 14<sup>th</sup> Street within the project limit as shown on plans.
- Streetscaping throughout the 14<sup>th</sup> Street corridor as shown in the plans.
- The installation of traffic signing and permanent pavement markings.
- Upgrading of street lighting throughout the 14<sup>th</sup> Street corridor as shown in the plans.
- Construction and upgrading of single catch basin, double catch basin, and triple catch basin.
- Construction / Upgrading of new Watermains, Fire Hydrants
- Full Reconstruction of R Street.
- Installation of new Bus Islands and bus pads as shown on the plans and as directed.
- The installation and use of erosion and sediment control measures as required.
- Mobilization and demobilization, performance of field layout, provision and maintenance of engineer's field facilities, progress photographs, and the proper maintenance of vehicular and pedestrian traffic during construction, including provision of all required construction warning and detour signs and traffic control devices.

## 2. STATUS OF CONSTRUCTION / PROGRESS SUMMARY

### Progress Summary:

1. Three days lost to adverse weather : 03/23,25 and 28
2. No progress on 12" water main tie-in still on hold by DCwater
3. Restore Various locations where T-base were removed
4. Pave From Corcoran to R street , Pave full intersection of R street all the way to Riggs St.
5. Paving T-U Block except location of water line Tie-in
6. Splicing Streetlights
7. Continue pulling Comm system cable from T to U street and to Reeves Center
8. Prepare for Switchover 1-100 pair at U street
9. Omni continue parging and cleaning their inlets
10. Permanent Striping from Corcoran to R street
11. Plant additional trees along the corridor
12. Remove existing Stumps and Trees per plan

### PM Community Outreach Activities:

13. TBA personnel continues to respond to questions that come through project portal.
14. Continue working with Businesses along R St. block. Red light Bar, Sette Osteria. Including milli and paving operations
15. Reply to public concerns regarding the Corona virus

**3. QC/ ISSUES / ACTION ITEMS**

- DCwater still has one more tie-in to complete the DCWater/Pepco change order work. They need to schedule but currently all shutdown are on hold due to Coronavirus emergency proclamation
- Multiple areas are unfinished that prevents the landscapers from completing their work (i.e. Cobble stone, PCC sidewalk, light pole and foundations).
- Issue with Comm cable that is too big still waiting for Florida
- FMCC has slowed down significantly now that they have the time extension sense of urgency seemed to have disappeared. Have asked multiple times to schedule their subcontractor to begin punch list work
- FMCC was notified that the trench repairs done at U street (Pepco) and Q street (water valves) must be done per the gold book standard
- Need resolution on change order # 9

**ACTION ITEMS. -**

Action	Description	Action By	Original Date	Expected Date	Status
001	Address the MOT, safety issues within the corridor.	FMCC/Kevin Felix	June 5, 2019	March 31, 2020	Ongoing
002	Provide written document showing the potential danger with the installation of the handles for the grate placed IFO Cleaners at 1329 14 <sup>th</sup> Street	FMCC/Cesar Casanova	July 30, 2019	March 31, 2020	Ongoing
003	Mr. Said Chestnut to contact Mr. Jermaine Quattlebaum and complete the punch list for DC Water work.	ATCS/Said Chestnut and DC Water/ Jermaine Quattlebaum	August 06, 2019	March 31, 2020	Ongoing
004	Showing DDOT the price difference of the luminaire with and without the glare shield.	FMCC Electrical	January 21, 2020	March 31, 2020	Ongoing
005	Submit the price proposal for reinstall of the blue historical signs	FMCC/Abdalla Elsheikh	January 21, 2020	March 31, 2020	Ongoing
006	Discussed internally for change order of the HAWK signal	FMCC Electrical	February 4, 2020	March 31, 2020	Ongoing
007	FMCC to remove all the trees per plan to allow Cooper Enterprise to start the planting	FMCC/Abdalla Elsheikh	February 4, 2020	March 31, 2020	Ongoing

**4. MEETINGS/ PROJECT COORDINATION**

- New Progress Meeting are schedule via teleconference every other Tuesday at 10:30am.

## 5. DAILY WORK PERFORMED

### Monday 03/23/2020

**FMCC** was onsite scheduling for electrical work at SEC of T Street and also tree removal along the corridor for Excel. Rain was commencing and keeping going. FMCC decided to cancel work and return the following date.

### Tuesday 03/24/2020

**FMCC** was onsite providing MOT devices for Asphalt crew at 14<sup>th</sup> St from Corcoran St to Riggs St

**FMCC Asphalt** was onsite for asphalt operation on 14<sup>th</sup> St from Corcoran to Riggs St. Saw joints were done including removal of asphalt debris via backhoe and broom truck. Tack coat was placed prior to all asphalt placement. Temperatures were checked with gauge and found to be compliant. (18) asphalt trucks delivered 457 Tons of asphalt was placed. Yellow and white temporary tape was placed for lane markings following asphalt placement. Asphalt was not completed at Corcoran St west of 14<sup>th</sup> St.

**Cooper Landscaping** worked from Thomas Circle to Corcoran St planting (21) Nuttall Oak trees and added planting soil at 1314B 14<sup>th</sup> St.

**Omni Excavators** was onsite cleaning catch basins throughout the corridor.

**Excel Tree Landscaping** was onsite removing (5) trees (2) Sawtooth Oak s(2000 14<sup>th</sup> St), (1) Red Oak (2300), (1) White Oak (1400), and Columnar English (1200).

### Wednesday 03/25/2020

**FMCC** was onsite scheduling for electrical work at from T Street to U Street. Rain was commencing and keeping going. FMCC decided to cancel work and return the following date.

### Thursday, 03/26/2020

**FMCC** was onsite providing MOT devices for work including:

- Paving work in the proximity of U Street and Corcoran Street with bike lanes at R Street and T Street.
- Tree installation, removal and root pruning at multiple locations (parking lanes taken).
- Pole removal along the corridor.
- Manhole cleanup and purging along the corridor on the northbound

**FMCC Electrical** crew was onsite scheduling work at SEC of Wallace Street pulling the cables. This work was cancelled and changed to pole removal along the corridor. Quantities will be verified and paid at the end of the month.

**FMCC Asphalt** was onsite for asphalt operation on 14<sup>th</sup> St at Corcoran to U St (with bike lane and some parking lanes). Saw joints were done including removal of asphalt debris via backhoe and broom truck. Tack coat was placed prior to all asphalt placement..

**Omni** performed manhole cleanup and purging along the corridor on the northbound of 14<sup>th</sup> Street.

**Excel Tree Landscaping** was onsite removing (1) Pin Oak tree with root pruning at 1931 14<sup>th</sup> Street NW.

**Cooper Enterprises** continued installing trees along the corridor, ten (10) Nuttall Oaks and seven (7) Swamp White Oaks, also two (2) Ilex Glabra (Densa) at Corcoran Street. Inspector was made aware that all Shumard and Scarlet Oak were substituted to Nuttall Oaks per Mr. Banua's agreement (UFA). Also, filled some plant bed soil in the proximity of P Street (1502, 1506, 1508, 1520 and 1521 14<sup>th</sup> Street NW)

### **Friday, 03/27/2020**

**FMCC** was onsite providing MOT devices for work including:

- Communication work at u Street Intersection
- Electrical work at W St and V St.
- DC-line Striping work Between Corcoran and R street

**Omni:** One crew was on site purging and adjusting the cover of the Catch basin south of Cochran. Part of DC Water punch list work

**FMCC Electrical** Crew was on W street and Florida Installing new light fixtures on the LP west side.

**FMCC Electrical (comm Crew)** crew was onsite starting work at SEC of T street pulling communication cable north To U street. They proceed with connection from U street to Reeve center. Pull 1-100 pair back to U Street TEC cabinet

**FMCC Civil** was on various locations placing sidewalk concrete left behind after removing the old T-Bases. Locations NEC T street, SEC V Street, SWC V Street, two bus shelters (T Street, R street).

**DC Line.** were on site Layout and Stripe crosswalk south portion of R street and Crosswalks of Corcoran, main line and bike lanes.

### **Saturday, 03/28/2020**

**FMCC** cancelled work due to adverse weather. ( Rain)

## 7. RFI's/SUBMITTALS

### 1. Requests for Information:

- To date, we have received **50** RFIs; **47** RFIs have been answered.
- Glare shield RFI submitted to streetlight division.
- Pending response about Hawk Signal material cost adjustment

### 2. Submittals:

- We have received **87** Submittals; **87** Submittals have been Approved.

## 8. CHANGE ORDERS/TASK ORDERS

- Price breakdown for add water work received from FMCC. Tie-in were priced separately. Pepco sent letter on 12/14 accepting and taking responsibility of the CO. Sent Article 3 letter to FMCC on 12.20. Received commitment from DCwater to write Change. Provided preliminary CO package to



Sam ( DDOT) to begin process. Quantity for Tie-in was estimated.

- FMCC Submitted a change order for 100K for max cell innerduct installed with fiber optic. Requesting a review from Wasim and Harvey group to check if it has merits.

## 9. DBE or CBE PARTICIPATION SUMMARIES

3. ATCS CBE / DBE Activity:
  - Hayat Brown LLC.: Provided Office Engineering and Inspection support for this project.
  - Cube root: Provided Inspection support
  - Tina Boyd- PR and Outreach support, webpage management
4. Fort Myer Construction Corp. DBE Activity:
  - Omni Excavators Inc.
  - Den United LLC.
  - DC Line
  - Cooper landscaping
  - Long Fence
  - Capital Flexible pavement
  - Driveway impressions

## 10. ACCIDENTS/INCIDENT

No incidents to report. FMCC was reminded to maintain DC emergency procedures to prevent the transmission of Cor-vid19.

## 11. PHOTOS OF WORK PERFORMED THIS PERIOD



FMCC placing asphalt SB 14<sup>th</sup> St near R St



R St west of 14<sup>th</sup> St asphalt placement completed



FMCC rolling and compacting 1700 block of 14<sup>th</sup> St SB





FMCC placing asphalt NB 14<sup>th</sup> St near R St



Cooper Landscaping at 1250 14<sup>th</sup> St placing trees





More trees to be placed between Thomas Circle and Corcoran St



A Section to be paved at Corcoran Street





Cooper Enterprises delivered trees to the site



Excel on site to remove some roots in the proximity of U Street





Tack coat for paving work at Corcoran Street



Paving work at Corcoran Street with truck





Omni was on site purging and cleaning the manholes



Repair Sidewalk SEC V Street.






Repair Sidewalk NEC T Street.



Omni Parging Manholes Corcoran Ave.



DC Line.- Layout of Crosswalk R street

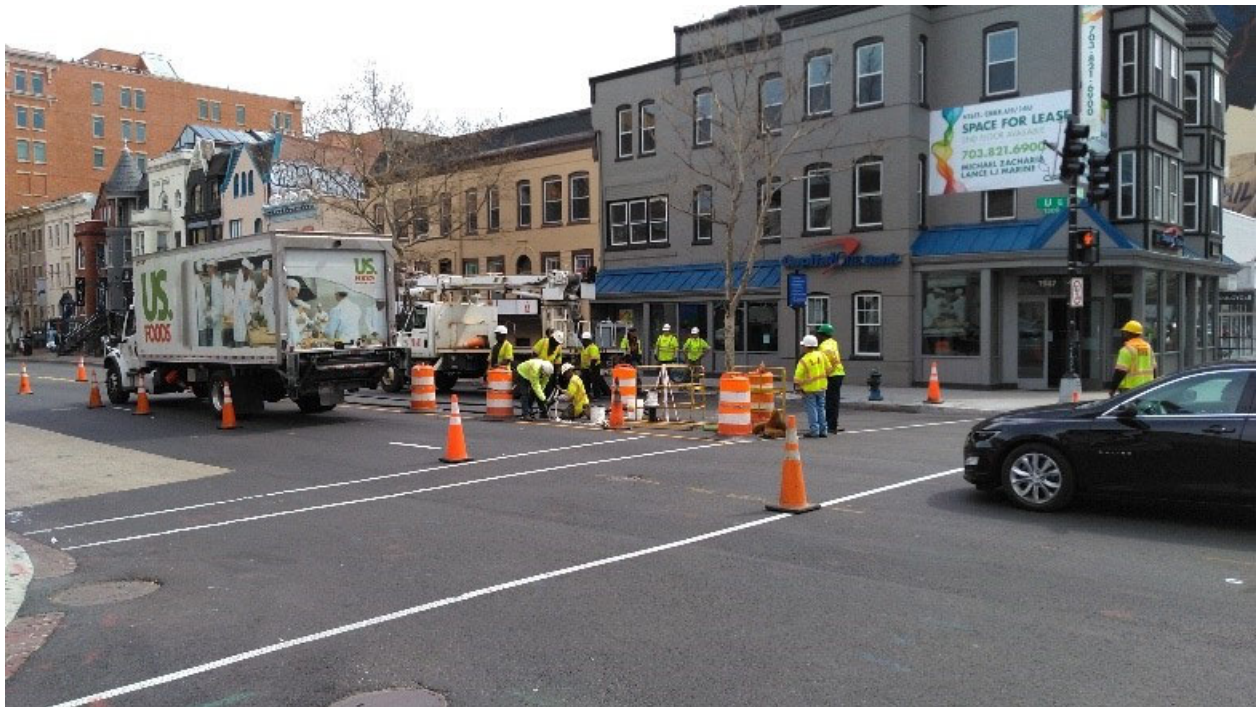

FMCC Electrical pulling 1-100 pair at U street
